Please provide the following information:

1. Provide overall height of the room.
2. Determine maximum drop. Measure from the underside of the canopy (NOT away from floor).
3. Determine L x W install dimensions.
4. Provide a sketch of the ideal distribution of pendants relative to the canopy.

Coaxial cable suspension system in a random configuration.

Coaxial cable will come in bags labeled with length in mm.
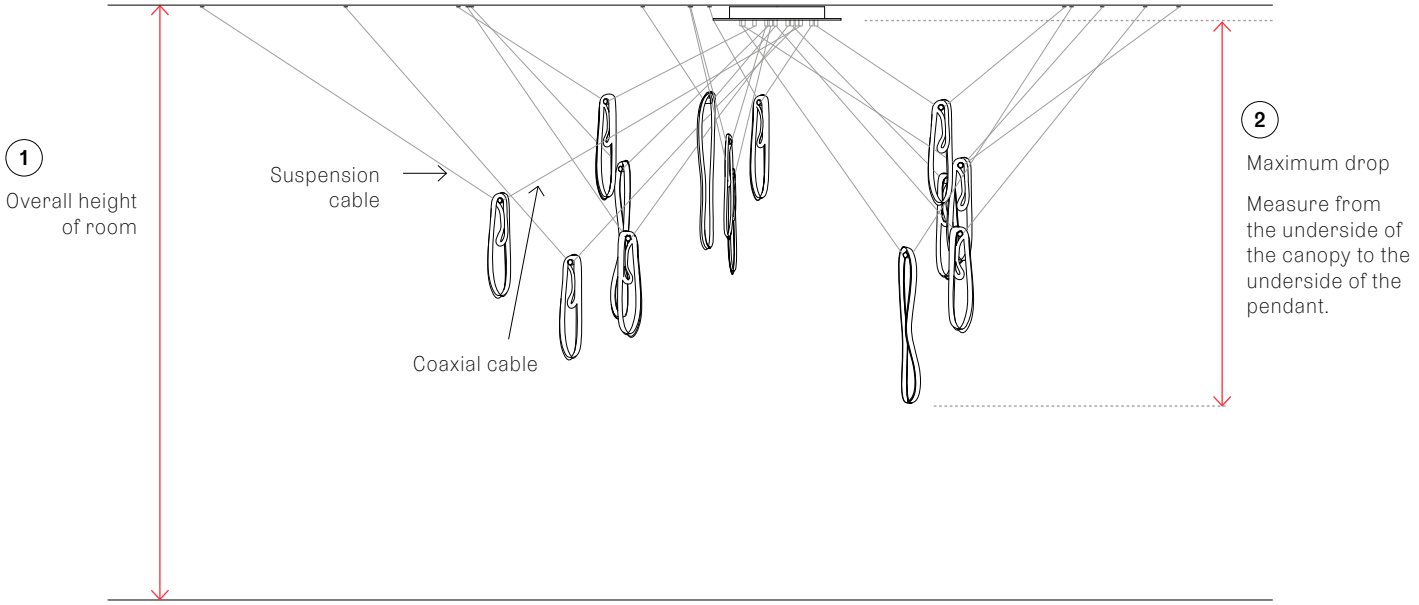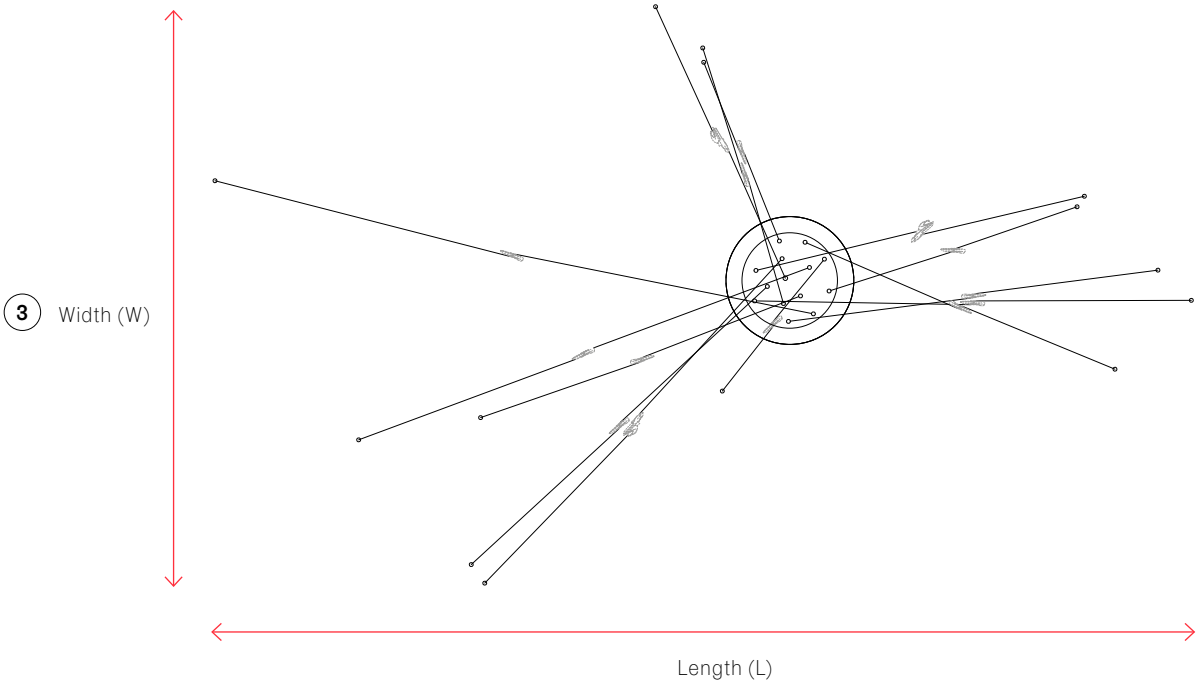
Suspension cable comes in 3m increments which are site adjustable. The length should be adjusted on-site to match to the length of the coaxial cable.
